GODDARD SPACE FLIGHT CENTER

EOS GROUND SYSTEM (EGS) TEST DETAIL
EGS TEST VERSION

LAST CHANGE 08/30/96
STATUS AS OF 08/30/96

Description (Responsible Org.)	Start	Finish
TRMM Engineering Version Science S/W Testing (ITs)		
TRMM Engineering Version Science S/W Testing	22MAR	12AUG
LaRC (CERES) Science S/W Testing	22MAR	12AUG
MSFC (LIS) Science S/W Testing	29MAR	18JUN
AM-1 Beta Version Science SW Testing (ITs)		
AM-1 Beta Version Science S/W Testing	18MAR	02JUL
LaRC (MISR) Science S/W Testing	22 01APR	02JUL
LaRC (MOPITT) Science S/W Testing	18APR	02JUL
GSFC (MODIS) Science S/W Testing	22MAR	25JUN
EDC (ASTER) Science S/W Testing	18MAR	02JUL
ECS IR-1/TSDIS Build 1 I&T and Eng Tests (SI&T)		
ECS IR-1/ TSDIS Build 1 I&T and Eng Tests	17APR	12DEC
ECS IR-1 / TSDIS B1 Eng Tests	17APR	01MAY
GSFC TSDIS B1 System and I/F Test	10JUN	(2) 30AUG 13NOV
GSFC TSDIS B1 Preliminary I/F Test	05APR 01MAY	17MAY
Fully Integrated Test #7	13JUN	(4) 10SEP 12SEP
Mission Sim #1	12JUL	(5) 04OCT 07OCT
GSFC TSDIS B1 AT and I/F Test	16SEP	(3) 28OCT 06DEC
EBnet TSDIS I/F Test	27SEP	(1) 14NOV 12DEC
EBnet Component Acceptance Testing (Code 540)		
EBnet Site I&T / TRMM Ready	26JUL	07NOV
F00 and Other Mission Integration Support (TBR)		
F00 and other Mission Integ Suppt. (TBR)	08OCT	29NOV
ASTER L1 Beta Science S/W Testing at EDC (TBR)	08OCT	29NOV

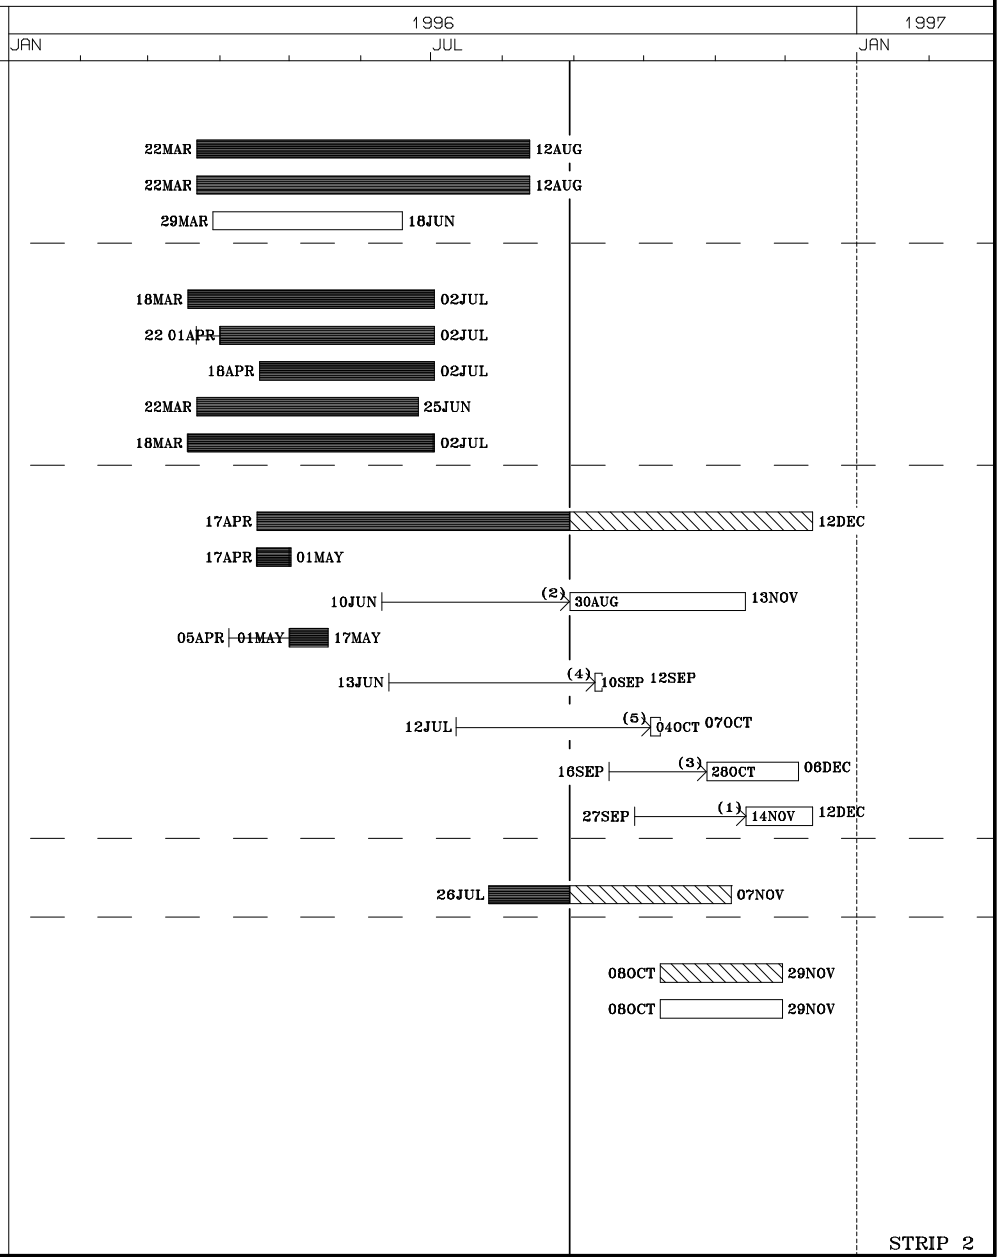

STRIP 2
